Upper Texas Coast Channels

Jack Otis

Project Manager

US Army Corps of Engineers

28 October 2010

Galveston District – 2010 Dredging Conference

Custodians of the Coast

US Army Corps of Engineers

BUILDING STRONG®

Upper Texas Coast Channels

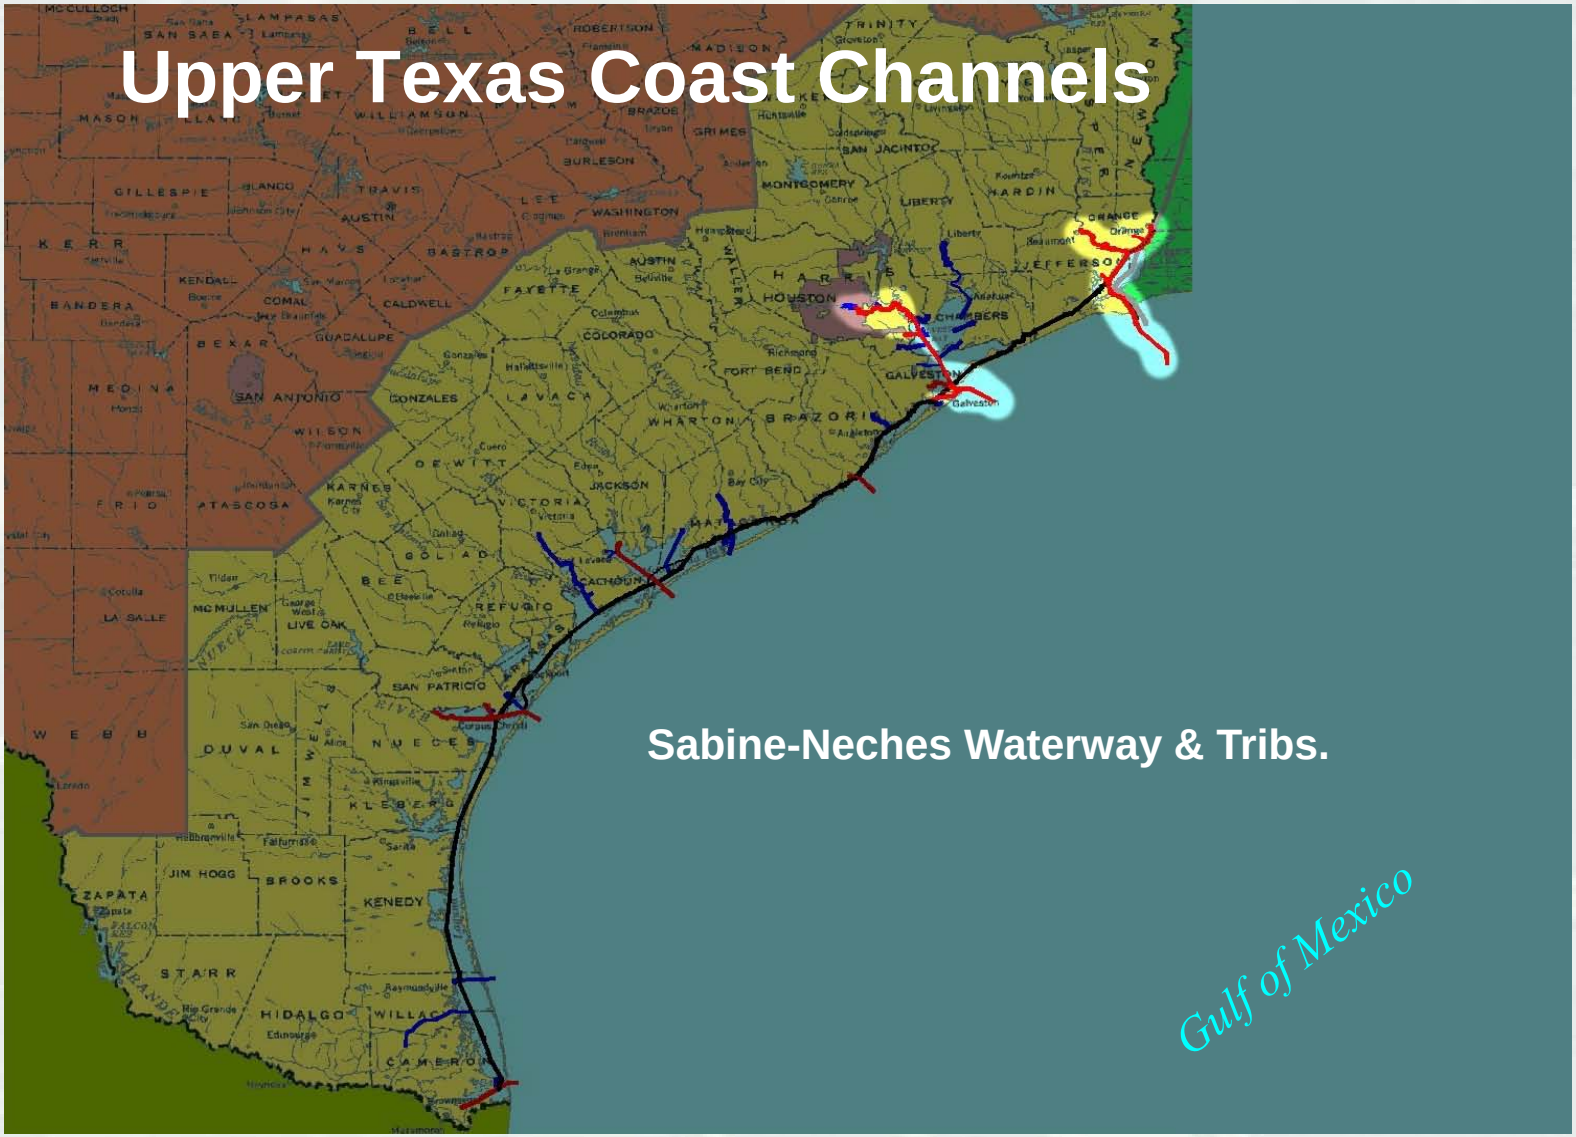

FY 2011

-Projects-

FY	Project	OPM	Quan	Drg. Type	Adv	Bids	Award	Dredging Start	Dredging End
2011	SABINE NECHES WATERWAY, TX Sabine Neches Canal	Jack Otis 409-766-3157	3,400,000	Pipeline	8-Apr-11	29-May-11	5-Jul-11	20-Jul-11	20-Nov-11
2011	SABINENECHES WATERWAY, TX Sabine Pass Channel	Jack Otis 409-766-3157	1,800,000	Hopper	3-Jun-11	5-Jul-11	14-Jul-11	25-Aug-11	26-Dec-11
2011	SABINENECHES WATERWAY, TX Sabine Neches and Canal, Dredge to Advanced Maintenance	Jack Otis 409-766-3157	1,720,000	Pipeline					
2011	SABINENECHES WATERWAY, TX Sabine Pass Channel, Dredge to Advanced Maintenance	Jack Otis 409-766-3157	5,037,000	Hopper					

Sabine Neches Waterway

Sabine-Neches Canal

- **Type of Work:** Maintenance Dredging
- **Depth:** 40’
- **Quantity:** 3,400,000 CY
- **Material Type:** Silt
- **Placement Plan:** PA-8 & 11
- **Avg. Distance to PA:** 1.5-2.0 Miles
- **Equipment Type:** Pipeline Dredge
- **Small Business Set Aside:** NA
- **Advertise:** 08 APR 2011

Sabine Neches Waterway

Sabine Pass Channel

- **Type of Work:** Maintenance Dredging
- **Depth:** 40’
- **Quantity**: 1,800,000 CY
- **Material Type:** Silt/Sand
- **Placement Plan:** Upland/Confined PA 5 & 6
- **Avg. Distance to PA:** 2.5-3.0 Miles
- **Equipment Type:** Pipeline Dredging
- **Small Business Set Aside:** NA
- **Advertise:** 03 JUN 2011

FY 2012

-Planned Requirements-

FY	Project	OPM	Quan	Drg. Type	Adv
2012	SABINE NECHES WATERWAY, TX DAMP of PA No. 8 & Incremental Northern Levee Raise	Jack Otis 409-766-3157	NA	Pipeline	10-Mar-12
2012	SABINE NECHES WATERWAY, TX PA Canal, Turning Basin & Junction and Taylor's Bayou	Jack Otis 409-766-3157	4,500,000	Pipeline	1-Jun-12
2012	SABINE NECHES WATERWAY, TX Sabine Neches Canal	Jack Otis 409-766-3157	1,720,000	Pipeline	8-Apr-12
2012	SABINE NECHES WATERWAY, TX Sabine Pass Channel	Jack Otis 409-766-3157	1,800,000	Pipeline	3-Jun-12
2012	SABINE NECHES WATERWAY, TX Sabine River Channel	Jack Otis 409-766-3157	900,000	Pipeline	5-May-12
2012	SABINENECHES WATERWAY, TX SNWW Outer Bar and Bank Channel	Jack Otis 409-766-3157	2,000,000	Hopper	3-Aug-11

Sabine Neches Waterway

Outer Bar and Bank Channel

- **Type of Work:** Maintenance
- **Depth:** 42’
- **Quantity:** 2,000,000 CY
- **Material Type:** Silt
- **Placement Plan:** Offshore
- **Avg. Distance to PA:** 2 Miles
- **Equipment Type:** Hopper Dredging
- **Small Business Set Aside:** NA
- **Advertise:** 01 OCT 11

Sabine Neches Waterway

Pt. Arthur Canal, Turning Basin & Junction Area

- **Type of Work:** Maintenance Dredging
- **Depth:** 40’
- **Quantity:** 4,500,000 CY
- **Material Type:** Silt
- **Placement Plan:** PA-8
- **Avg. Distance to PA:** 1.5-2 miles
- **Equipment Type:** Pipeline Dredging
- **Small Business Set Aside:** NA
- **Advertise:** 01 MAR 12

Questions Comments?

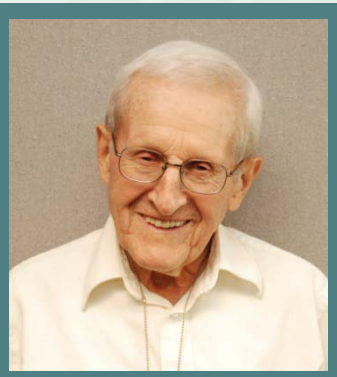

For more information, contact:

Jack Otis
Project Manager

Project Management Branch, Programs & Project Management Division
U.S. Army Corps of Engineers, Galveston
409-766-3157
john.j.otis@usace.army.mil

Gulf of Mexico
